













## Roadway Improvements

- Gateway structure
  - Artist collaboration meeting
  - Concept
- Coggeshall Street plaza
- Pedestrian friendly area
- Reduce traffic speeds

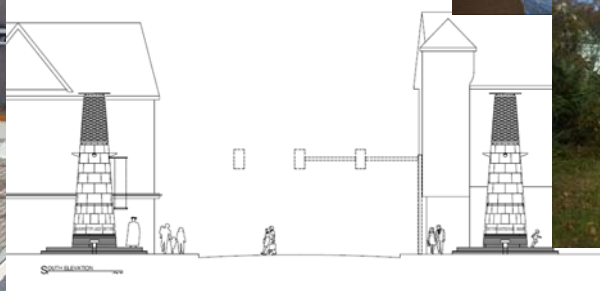


## Where Is The Work Going To Occur?

- Coggeshall Street to Holly Street – Utility Work
- Coggeshall Street to Sawyer Street – Roadway Improvements
- Utility work followed-up with roadway improvements
- 6-phases of work

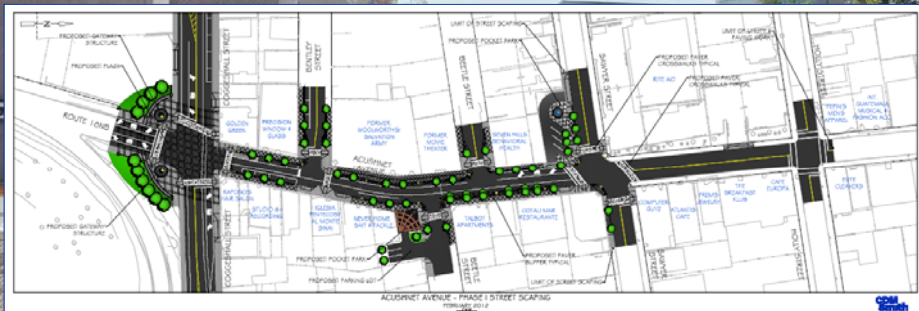


## What about traffic and detours?

- Work in City streets
  - Work on a block-by-block basis
  - Detours around work zones
- Temporary two-way traffic
- Sidewalk access
- Delivery Schedule

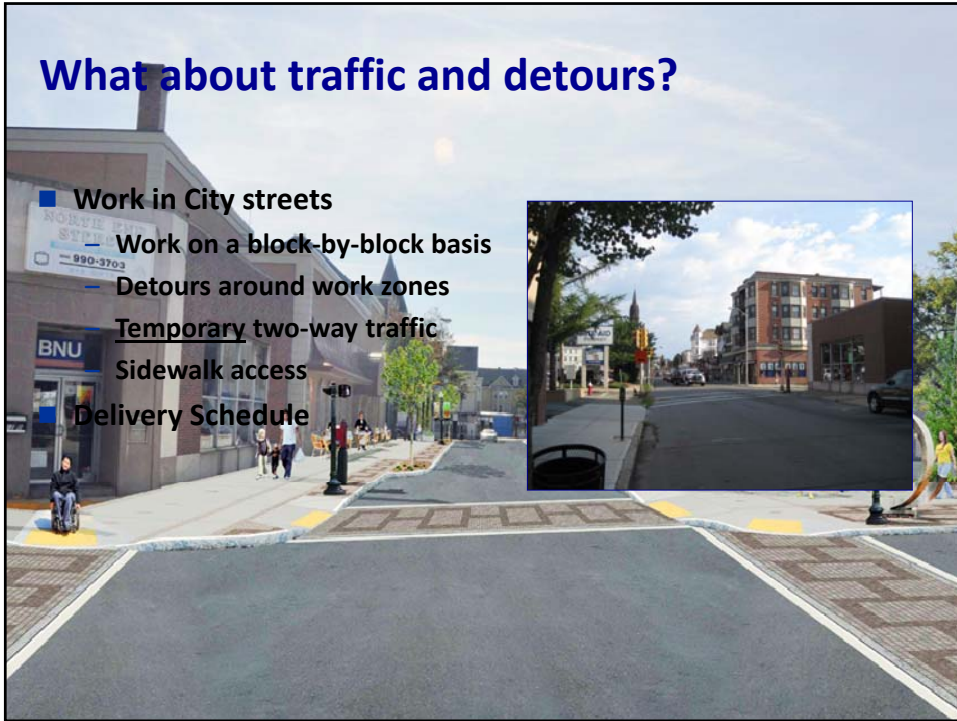

## Traffic and detours (cont.)

- Work at Coggeshall Street and Acushnet Avenue
  - Intersection closed
  - Detour to Route 195 and Belleville Avenue
- Shorten construction duration

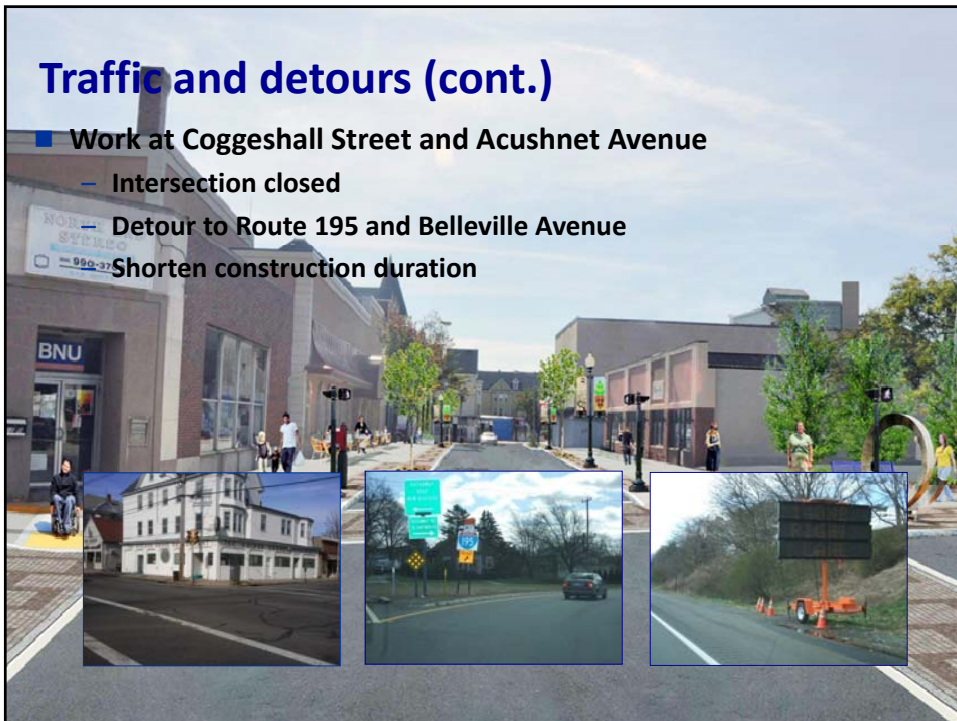

## When Will Project Begin and End?

- Phase 1 – 2 to 3 months
- Phase 2 – 1 to 2 months
- Phase 3 – 2 months
- Phase 4 – 3 to 4 months
- Phase 5 – 3 to 4 months
- Phase 6 – 5 to 6 months

- Project will begin in March 2012 and end in June 2013
- Utility work followed by street improvements
- Gap to allow for trenches to settle

Work Area	2012												2013												Duration
	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec			
Phase 1	█																						2 to 3 months		
Phase 2			█																					1 to 2 months	
Phase 3					█				█														2 months		
Phase 4							█														3 to 4 months				
Phase 5									█				█												3 to 4 months
Phase 6													█												5 to 6 months

## Work Hours and Restrictions

- Work Hours
  - City Streets: 7:00 a.m. to 5:00 p.m.
- Work Restrictions
  - Day of Portugal Feast
  - Feast of Blessed Sacrament
  - On-going City Projects



Photo by Feast of Blessed Sacrament - 2009



Photo by WordPress.com.



